

P CONSTRUCTION UPDATE

July 12th, 2019

PEWAUKEE
SCHOOL DISTRICT

SAFETY:

- Stay Hydrated as Temperatures Rise
- Hydro-Excavated Existing Utility Lines Prior to Excavation
- Zero (0) Accidents Since Project Start on 6/24

PROGRESS THIS WEEK:


- Obtained DNR Notice of Intent for Horizon and Pond Work to Begin
- Began Excavation at Horizon and Mobilized Concrete Foundation Crews
- We Energies Relocated Gas the Line Around the Horizon Addition



Placed Concrete Footings at Horizon

GOALS NEXT 2 WEEKS:

- Complete Foundation Work for Masonry Wall Construction to Begin
- Begin Site Utility Work Around the Loop Road and North Side of Horizon
- Establish Onsite Construction Office
- Commence Review of Bid Package 2 Bids

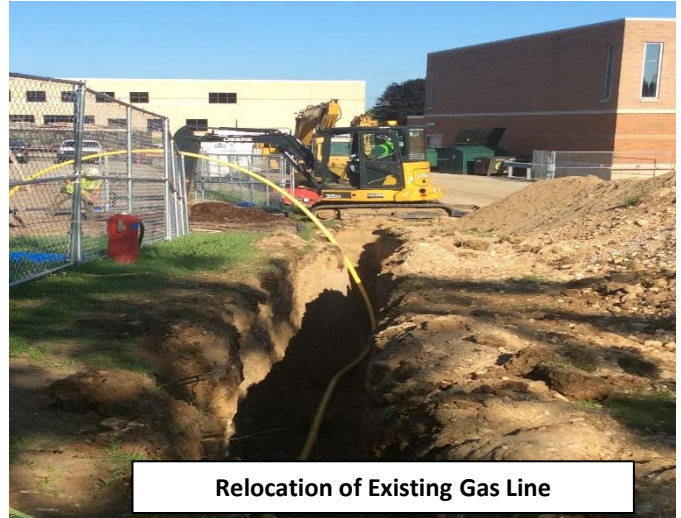

Relocation of Existing Gas Line

MILESTONE DATES:

- Bid Package 2 Bids Due – July 19th
- Last Day Summer School – July 19th
- 2019/2020 School Year Start – August 26th



Current Gymnasium Footprint

CONSTRAINTS:

- Public Sanitary & Water Permit Approvals
