



# CONSTRUCTION UPDATE

July 26<sup>th</sup>, 2019

**PEWAUKEE**  
SCHOOL DISTRICT

## SAFETY:

There will continue to be a lot of construction truck and equipment traffic along the campus ring road. Please stay in dedicated parking and walking areas.

## PROGRESS THIS WEEK:

### HORIZON

- Gym foundations & backfill completed
- Masonry wall work started

### SITE

- Storm detention pond excavation continued
- Storm utility piping along ring road started

## GOALS NEXT 2 WEEKS:

### HORIZON

- Masonry wall work to complete
- Precast wall panels to start

### SITE

- Storm detention clay liner to start
- Storm utility piping along ring road started

## MILESTONE DATES:

**2019/2020 School Year Start – August 26<sup>th</sup>**

### HORIZON

- Precast Start – Mid August


## CONSTRAINTS:

### HORIZON


- None

### SITE

- Public Sanitary & Water Permit Approvals
- Existing Utility Conflicts With New Storm Sewer

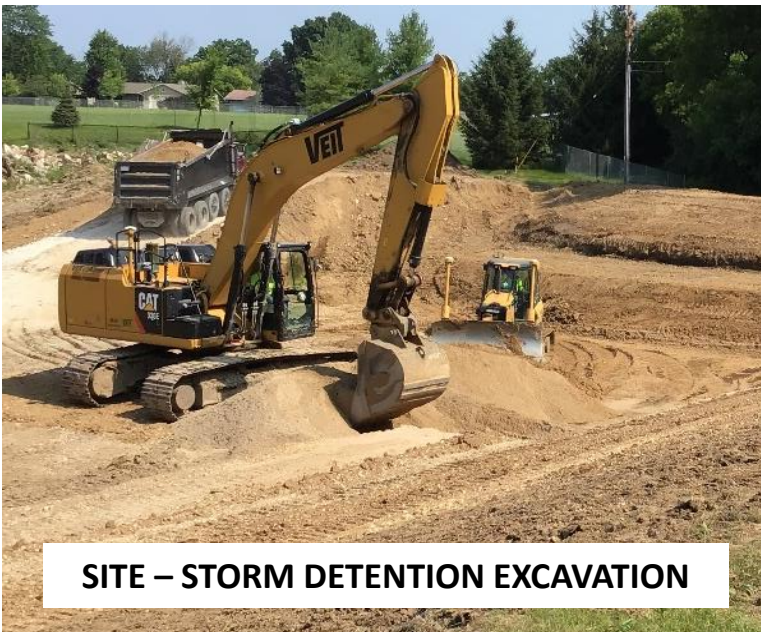

**SITE – STORM DETENTION EXCAVATION**

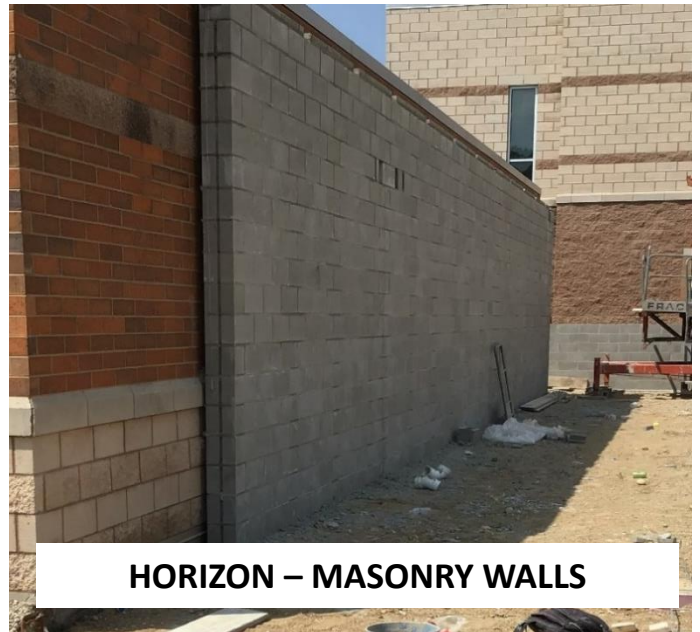

**HORIZON – MASONRY WALLS**
