

P CONSTRUCTION UPDATE

PEWAUKEE
SCHOOL DISTRICT

March 20th, 2020

SAFETY:

The health and safety of our staff and clients is always our top priority. CG Schmidt has taken steps to help prevent the spread of COVID-19 throughout our jobsite and the buildings we are working in. We have met with our subcontractors to inform them of the changes that we have made on site, including limiting access to the existing buildings that we are not actively working in and installing hand sanitizer stations for the employees that do have to enter the building.

WHAT YOU MAY NOTICE ON SITE IN THE NEXT WEEK:

PLE

- Crews will be finishing up the PLE Addition
- New demo will begin in the central classrooms

PROGRESS SINCE LAST UPDATE:

PLE

- ADDITION

- **MEP** - Completed finish installation
- **Bathrooms** - Installed toilet partitions

- RENOVATION

- **Demolition** - Began demolition in the central classrooms

ASA

- 6th GRADE ADDITION

- **MEP** - Finished rough-in work on the second floor
- **Paint** - Continued painting
- **Ceilings** - Continued installing grid
- **Drywall** - Continued installing soffits and bathroom walls
- **Ceramic Tile** - Began installing tile for bathroom floors

- INNOVATION ADDITION

- **Masonry** - Continued block walls
- **Precast Concrete** - Began installing second floor concrete

PHS

- **Canopy** - Continued demo and began installing structural steel
- **Concrete** - Continued slab on grade prep

ASA

- A crane will be on site to finish precast concrete installation at the Innovation Addition

PHS

- Concrete trucks will be in the loop during the day to pour the slabs at the addition

GOALS NEXT 2 WEEKS:

PLE

- ADDITION

- **Doors** - Install doors and hardware
- **Windows** - Install blinds
- **Cleaning** - Perform final cleaning
- **Turnover** - Begin punch list to complete minor tasks

- RENOVATION

- **Demolition** – Continue demo in central classrooms

ASA

- 6th GRADE ADDITION

- **MEP** - Install MEP fixtures & finishes
- **Paint** - Finish painting
- **Ceilings** - Finish grid and begin tiles
- **Drywall** - Finish installation
- **Ceramic Tile** - Continue installing bathroom tile

- INNOVATION ADDITION

- **Masonry** - Continued block walls
- **Precast Concrete** - Finish installing second floor

PHS

- **Masonry** - Begin interior walls
- **Concrete** - Pour 2nd floor topping slab and slab on grade
- **Canopy** - Continue structural framing

P CONSTRUCTION UPDATE

PEWAUKEE
SCHOOL DISTRICT

March 20th, 2020




PLE Addition - Bathroom



PLE Addition - Corridor



Asa 6th Grade Addition Cabinets and Light Fixtures

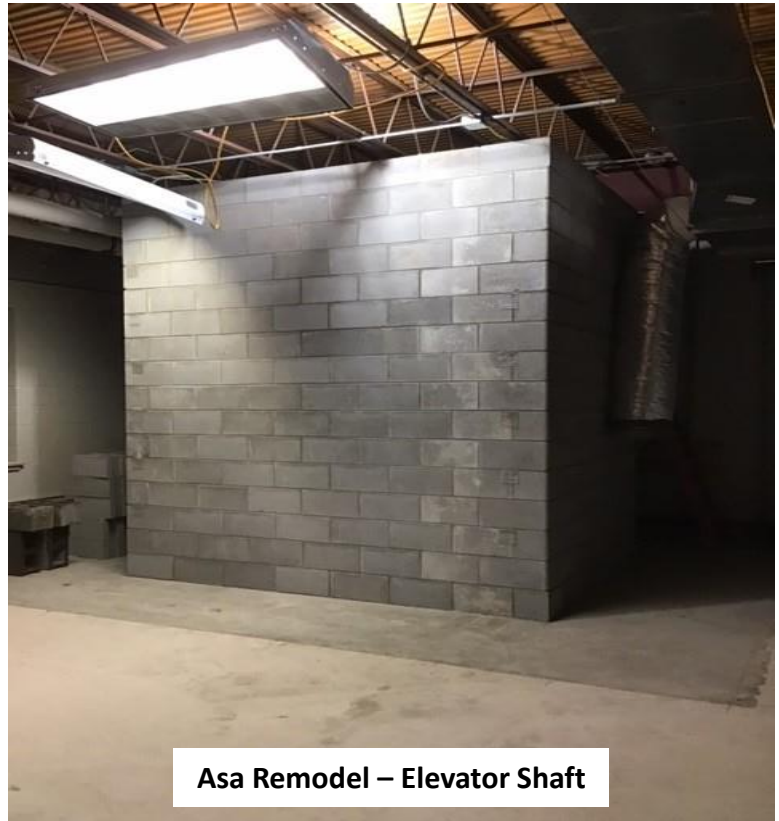

Asa Remodel – Elevator Shaft
