

## SAFETY:

The health and safety of our staff and clients is always our top priority. CG Schmidt has taken steps to help prevent the spread of COVID-19 throughout our jobsite and the buildings we are working in. We have met with our subcontractors to inform them of the changes that we have made on site, including limiting access to the existing buildings that we are not actively working in and installing hand sanitizer stations for the employees that do have to enter the building.

## WHAT YOU MAY NOTICE ON SITE IN THE NEXT WEEK:

### PLE

- Masonry walls installed in music and art rooms

### Site

- Curb and gutter to be installed between Horizon and 6<sup>th</sup> Grade Addition

### ASA

- Roof joists & metal decking being installed

### PHS

- Masons will be on the exterior of the building installing brick veneer

## PROGRESS SINCE LAST UPDATE:

### PLE RENOVATION

- **Demolition** - Continued demolition
- **Floors** - Continued epoxy flooring
- **Floors** - Installed new subfloor
- **Masonry** - Built block walls in music and art rooms

### ASA 6<sup>th</sup> GRADE ADDITION

- **Ceramic Tile** - Finished installing tile in bathrooms
- **MEP** – Started roof top HVAC unit

### - INNOVATION ADDITION

- **Iron Work** - Began installing roof joists
- **Masonry** - Started first floor masonry walls
- **Concrete** - Poured slab on grade
- **Insulation** - Spray foamed exterior of building

### PHS

- **MEP** - Rough in work continues
- **MEP** – Roof top units set
- **Masonry** - Began brick veneer and interior walls
- **Demo** – Began demo of the Tech Ed room
- **Demo** – Started main stair demolition

## GOALS NEXT 2 WEEKS:

### PLE

#### - ADDITION

- **Turnover** - Punchlist to complete minor tasks

#### - RENOVATION

- **Bathrooms** - Complete bathroom renovations
- **Drywall** – Wall framing in central classrooms

### ASA

#### - 6<sup>th</sup> GRADE ADDITION

- **Floor** - Finish flooring in corridors
- **Ceramic Tile** - Finish bathroom tile
- **Turnover** - Punchlist to complete minor tasks

#### - INNOVATION ADDITION

- **Masonry** - Continue 2<sup>nd</sup> floor interior block
- **MEP** – Work on overhead rough-in
- **Roofing** – Begin rubber roof
- **Concrete** - Pour topping slab on 2<sup>nd</sup> floor


### PHS

- **Masonry** - Continue exterior veneer
- **Drywall** – Begin framing walls on 2<sup>nd</sup> floor
- **Drywall** – Drywall 1<sup>st</sup> floor offices

# P CONSTRUCTION UPDATE

PEWAUKEE  
SCHOOL DISTRICT

April 17<sup>th</sup>, 2020

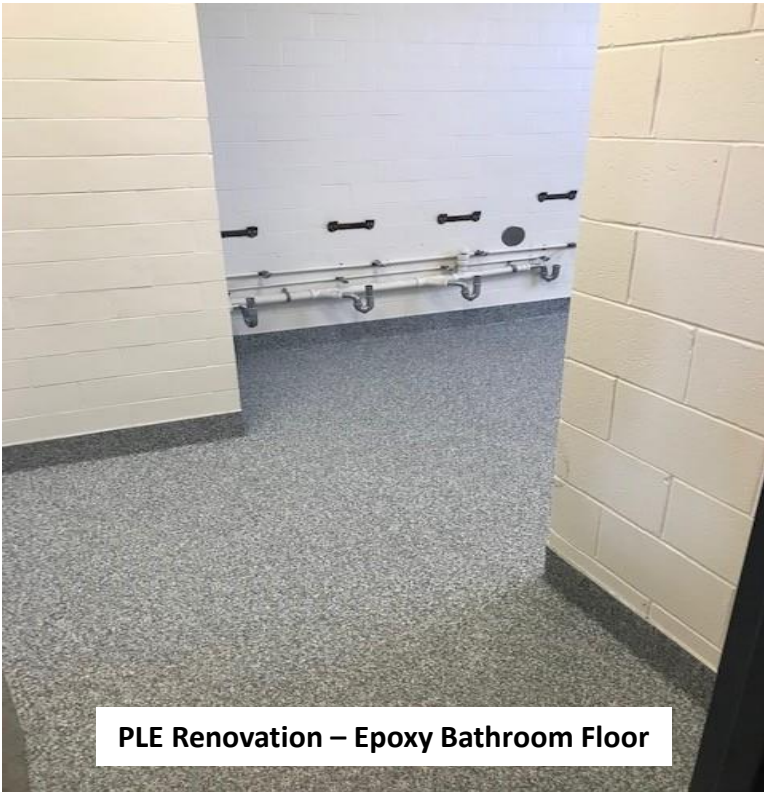


PLE Renovation – Epoxy Bathroom Floor



PLE Renovation – Music Room Masonry Walls



Horizon – Playground Subgrade

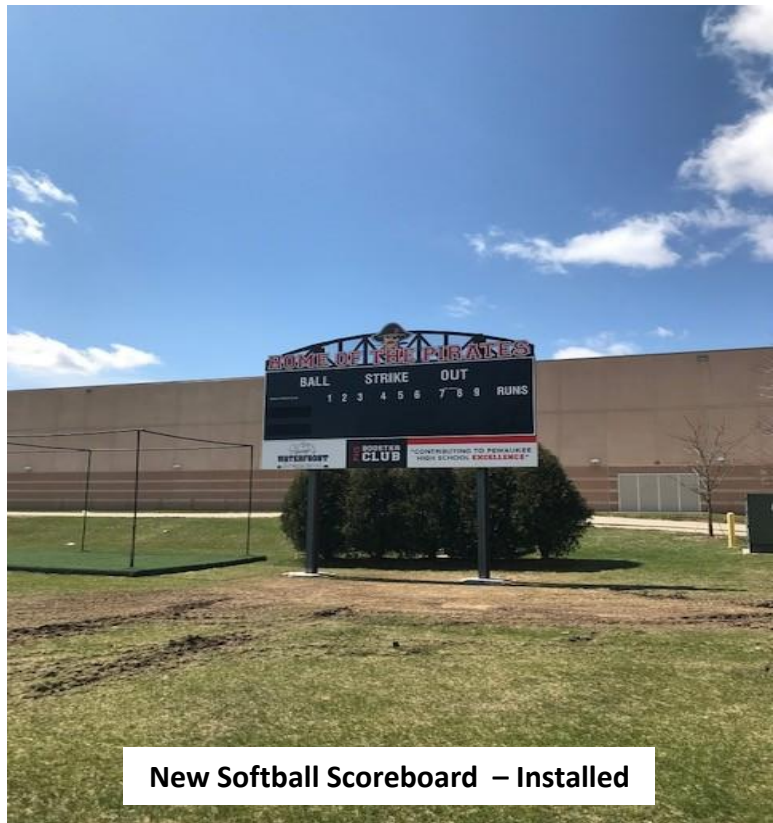

New Softball Scoreboard – Installed




# P CONSTRUCTION UPDATE

PEWAUKEE  
SCHOOL DISTRICT

April 17<sup>th</sup>, 2020



ASA Innovation Addition – Roof Joists Installed

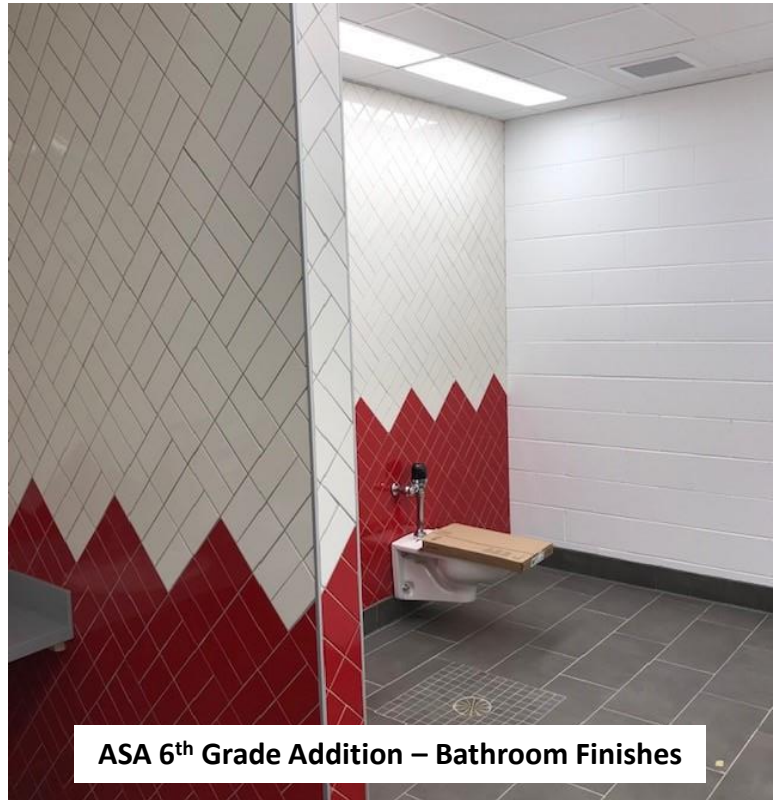

ASA 6<sup>th</sup> Grade Addition – Bathroom Finishes



ASA Innovation Addition – First Floor Masonry Wall



PHS Renovation – Tech Ed Demo
