

SAFETY:

The health and safety of our staff and clients is always our top priority. CG Schmidt has taken steps to help prevent the spread of COVID-19 throughout our jobsite and the buildings we are working in. We have met with our subcontractors to inform them of the changes that we have made on site, including a 100% glove policy, mask policy (when working within six feet of other people). Hand sanitizer stations are also installed around the site for everyone's use.

WHAT YOU MAY NOTICE ON SITE IN THE NEXT WEEK:

PLE

- Continued demo in area E

Site

- Pour sidewalk going in ASA 6th grade

ASA

- Finish installing flooring on 2nd floor addition
- ### Pewaukee High School
- Mechanical and Plumbing continuing install

PROGRESS SINCE LAST UPDATE:

PLE RENOVATION

- **Demolition** – Continued demo for Makers and existing Art room
- **Fire Protection** – Sprinkler systems are being installed
- **Flooring** – Installed epoxy and tile flooring

ASA 6th GRADE ADDITION

- **Demolition** – Finished demolition of cafeteria
- **Carpeting** – Finished first floor carpeting
- **Iron Work** – Finished installing structural steel

- INNOVATION ADDITION

- **Iron Work** – Metal roof decking installed
- **Masonry** – Started 2nd floor masonry walls
- **HVAC** – Continued installing ductwork

Pewaukee High School

- **Windows** – Began installing North facing windows
- **Framing** – Steel stud framing continues in 2nd floor Learning Commons
- **Paint** – Finish first floor office paint
- **Demo** – Finished Main office demo

GOALS NEXT 2 WEEKS:

PLE

- ADDITION

- **Turnover** – Punchlist work

- RENOVATION

- **Bathrooms** – Complete bathroom renovations
- **Demolition** – Continued demo of classrooms

ASA

- 6th GRADE ADDITION

- **Floor** – Finish flooring in 2nd floor corridor
- **Glass** – Install sliding glass doors
- **Turnover** – Punchlist work

- INNOVATION ADDITION

- **Masonry** – Continue 2nd floor interior block
- **MEP** – Work on overhead rough-in
- **Roofing** – Finish rubber roof

Pewaukee High School

- **Elevator** – Begin elevator install
- **Drywall** – Begin framing walls on 2nd floor
- **Structural Demo** – Cut open skylight

P CONSTRUCTION UPDATE

PEWAUKEE
SCHOOL DISTRICT

May 15th, 2020



PLE Renovation – 2nd Grade Classroom Demo



PLE Renovation – Existing Art Room Demo



PLE Renovation – Bathroom Epoxy Floors



PHS – Sheet Metal And Windows Installed


P CONSTRUCTION UPDATE

PEWAUKEE
SCHOOL DISTRICT

May 15th, 2020



PHS – Office Area Painted

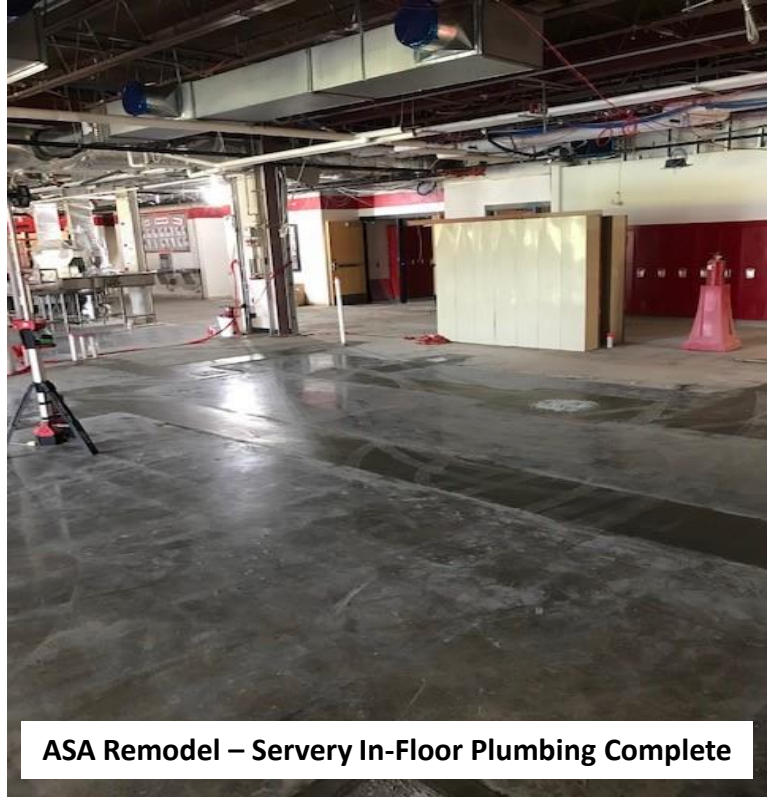

ASA Remodel – Servery In-Floor Plumbing Complete



ASA – Courtyard Window Install



ASA Remodel – 8th grade Ceiling Remodel
