

SAFETY:

The health and safety of our staff and clients is always our top priority. CG Schmidt has taken steps to help prevent the spread of COVID-19 throughout our jobsite and the buildings we are working in. We have met with our subcontractors to inform them of the changes that we have made on site, including a 100% glove policy, mask policy (when working within six feet of other people). Hand sanitizer stations are also installed around the site for everyone's use.

WHAT YOU MAY NOTICE ON SITE IN THE NEXT WEEK:

PLE

- Continue to install flooring in 4K/5K classrooms

Site

- Begin paving main parking lot

ASA

- Finish drywall in the new administrative area

Pewaukee High School

- Masonry walls will start to go up in the high school entrance

PROGRESS SINCE LAST UPDATE:

PLE RENOVATION

- **Drywall** – Installed ceiling clouds in music and art rooms
- **Fire Protection** – Continued sprinkler installation
- **Masonry** – Began masonry walls in 4K area

ASA Clark Remodel

- **HVAC** – Continued installing ductwork
- **Drywall** – Continued drywall installation in administrative area
- **Framing** – Finished stud framing for lockers by the Seryery
- **Framing** – Finished stud framing in Administrative area

INNOVATION ADDITION

- **HVAC** – Continued installing ductwork
- **Plumbing** – Continued installing plumbing
- **Stairs** – Began installing stair case leading to 2nd floor Resource area

Pewaukee High School

- **Plumbing** – Continued installing in floor plumbing
- **Carpet** – Finished installing carpet in main office area
- **Concrete** – Filled in the rest of the footing openings in the existing main office area

GOALS NEXT 2 WEEKS:

PLE

- RENOVATION

- **Renovation** – Complete district office remodel
- **Demolition** – Substantially complete with demo
- **Masonry** – Finish masonry walls completely

ASA

- 6th GRADE ADDITION

- INNOVATION ADDITION

- **Masonry** – Finish 1st floor interior block
- **MEP** – Finish overhead rough-in
- **Framing** – Start framing in the new addition
- **Drywall** – Begin drywalling in the new addition

Pewaukee High School

- **Elevator** – Finish framing elevator entrance
- **Demolition** – Substantially complete with demo
- **Skylight** – Install skylight
- **Masonry** – Finish installing block walls


P CONSTRUCTION UPDATE

PEWAUKEE
SCHOOL DISTRICT

June 19th, 2020




PLE Renovation – Ceiling Clouds Installed

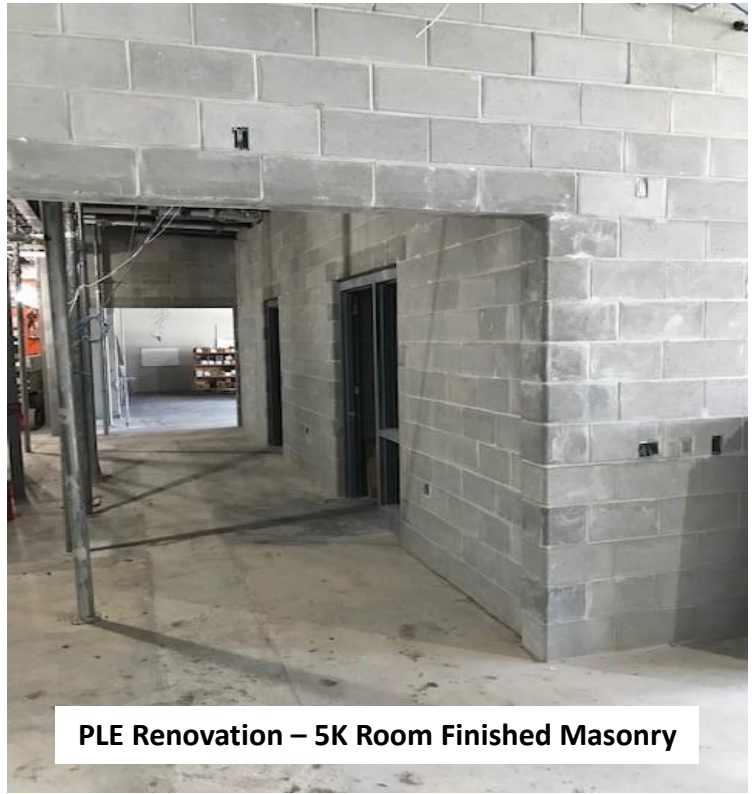

PLE Renovation – 5K Room Finished Masonry



PLE Renovation – 4K/5K Flooring Installed

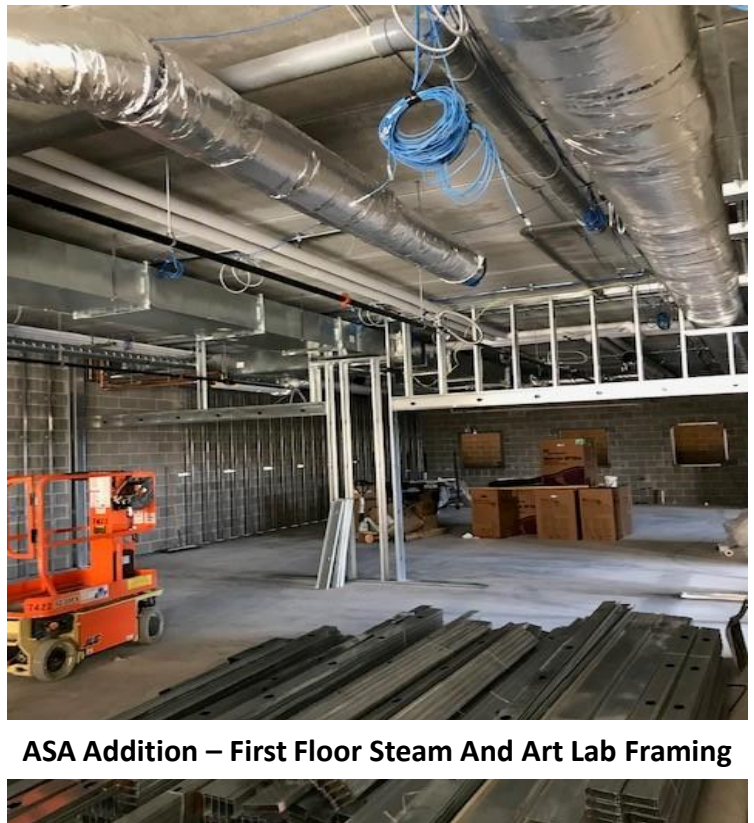


ASA Addition – First Floor Steam And Art Lab Framing

P CONSTRUCTION UPDATE

PEWAUKEE
SCHOOL DISTRICT

June 19th, 2020

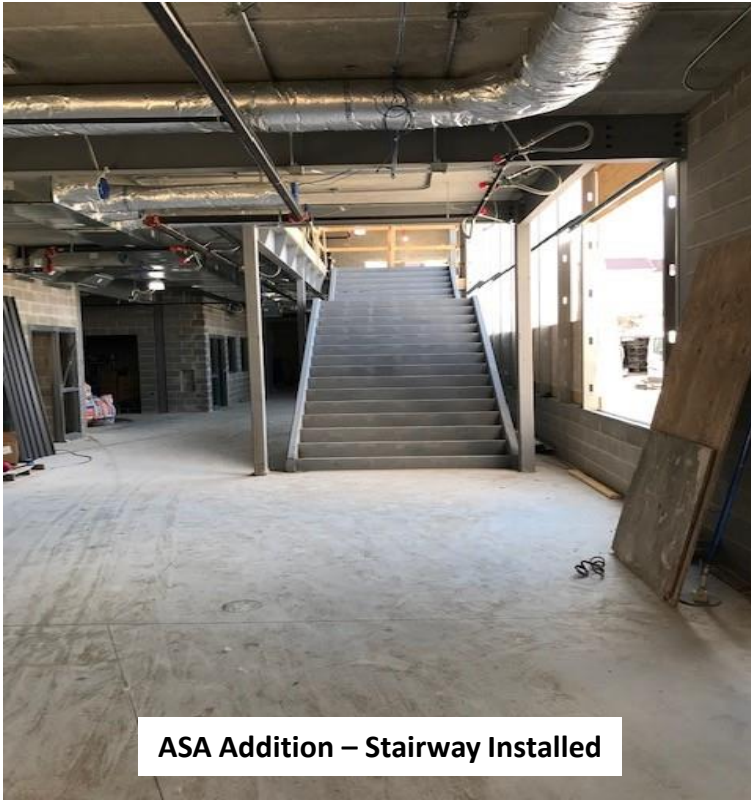

ASA Addition – Stairway Installed



PHS – Main Office Carpet Installed



PHS Entrance – Prep For Masonry Walls



PSD Campus – Islands Mulched And Trees Planted
